


Český rozhlas - Římská 15  
rekonstrukce VZT, klimatizace a vytápění



Český rozhlas - Římská 15  
rekonstrukce VZT, klimatizace a vytápění

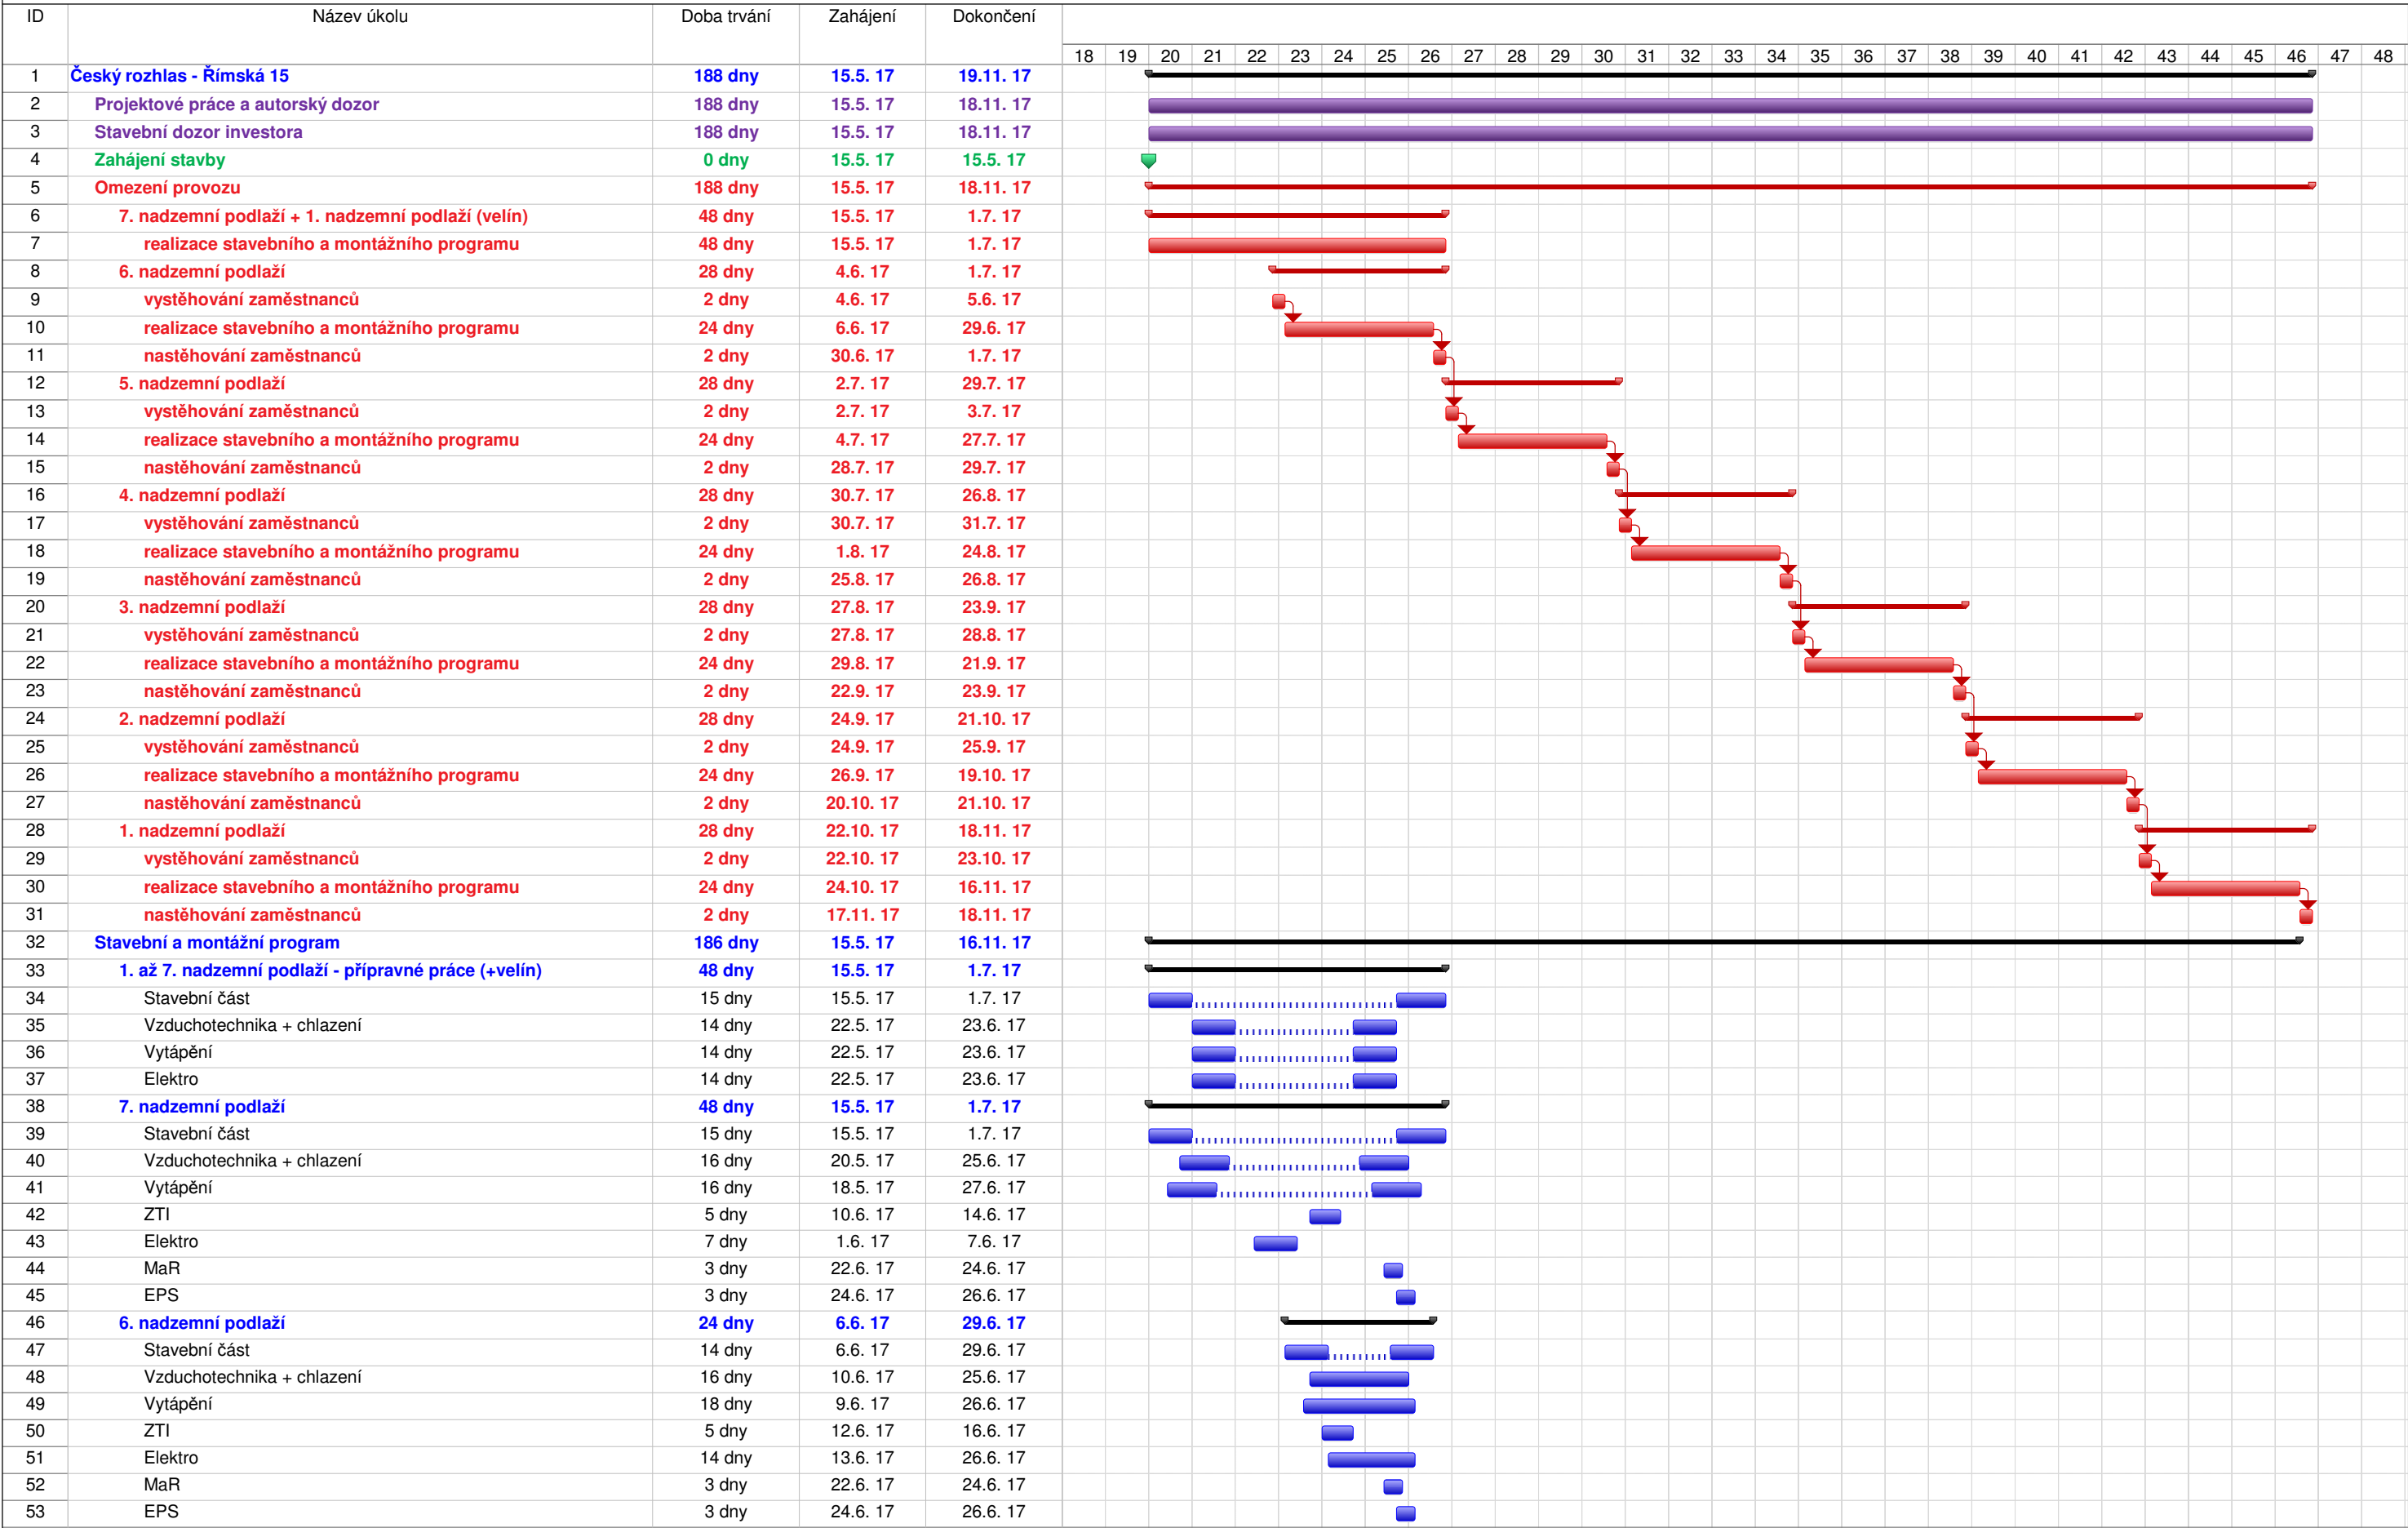

ID	Název úkolu	Doba trvání	Zahájení	Dokončení	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48
54	5. nadzemní podlaží	24 dny	4.7. 17	27.7. 17																															
55	Stavební část	14 dny	4.7. 17	27.7. 17																															
56	Vzduchotechnika + chlazení	16 dny	8.7. 17	23.7. 17																															
57	Vytápění	18 dny	7.7. 17	24.7. 17																															
58	ZTI	5 dny	10.7. 17	14.7. 17																															
59	Elektro	7 dny	11.7. 17	17.7. 17																															
60	MaR	3 dny	20.7. 17	22.7. 17																															
61	EPS	3 dny	22.7. 17	24.7. 17																															
62	4. nadzemní podlaží	24 dny	1.8. 17	24.8. 17																															
63	Stavební část	14 dny	1.8. 17	24.8. 17																															
64	Vzduchotechnika + chlazení	16 dny	5.8. 17	20.8. 17																															
65	Vytápění	18 dny	4.8. 17	21.8. 17																															
66	ZTI	5 dny	7.8. 17	11.8. 17																															
67	Elektro	7 dny	8.8. 17	14.8. 17																															
68	MaR	3 dny	17.8. 17	19.8. 17																															
69	EPS	3 dny	19.8. 17	21.8. 17																															
70	3. nadzemní podlaží	24 dny	29.8. 17	21.9. 17																															
71	Stavební část	14 dny	29.8. 17	21.9. 17																															
72	Vzduchotechnika + chlazení	16 dny	2.9. 17	17.9. 17																															
73	Vytápění	18 dny	1.9. 17	18.9. 17																															
74	ZTI	5 dny	4.9. 17	8.9. 17																															
75	Elektro	7 dny	5.9. 17	11.9. 17																															
76	MaR	3 dny	14.9. 17	16.9. 17																															
77	EPS	3 dny	16.9. 17	18.9. 17																															
78	2. nadzemní podlaží	24 dny	26.9. 17	19.10. 17																															
79	Stavební část	14 dny	26.9. 17	19.10. 17																															
80	Vzduchotechnika + chlazení	16 dny	30.9. 17	15.10. 17																															
81	Vytápění	18 dny	29.9. 17	16.10. 17																															
82	ZTI	5 dny	2.10. 17	6.10. 17																															
83	Elektro	7 dny	3.10. 17	9.10. 17																															
84	MaR	3 dny	12.10. 17	14.10. 17																															
85	EPS	3 dny	14.10. 17	16.10. 17																															
86	1. nadzemní podlaží	24 dny	24.10. 17	16.11. 17																															
87	Stavební část	14 dny	24.10. 17	16.11. 17																															
88	Vzduchotechnika + chlazení	16 dny	28.10. 17	12.11. 17																															
89	Vytápění	18 dny	27.10. 17	13.11. 17																															
90	ZTI	5 dny	30.10. 17	3.11. 17																															
91	Elektro	14 dny	31.10. 17	13.11. 17																															
92	MaR	3 dny	9.11. 17	11.11. 17																															
93	EPS	3 dny	11.11. 17	13.11. 17																															
94	Ukončení stavby	0 dny	19.11. 17	19.11. 17																															
